


Dear Residents:

After years of meetings and design, the Donohue Drain Project is scheduled to commence Tuesday, December 1st. The selected contractor will be mobilizing on Monday, November 30th with construction to begin on Tuesday, December 1st. The project will start with the installation of the new Lake outlet at the west end of the lake crossing under Walnut Lake Road. The road will be closed for two weeks. Attached is a construction schedule and a road closure schedule. We have been assured that proper detours and signage will be provided. All schedules are subject to change based on weather conditions.


John Aitken from the Oakland County Water Resource Commission has been assigned as the inspector and the Project Manager is Karen Warren (phone 248-858-0598). John Roda and Marshall Labadie will be inspecting on behalf of the Township pursuant to the Wetland Review Board permit conditions and as needed.



Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	2010																	
						JUN			JUL			AUG			SEP			OCT					
						14	21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	04	11

Channel Rehabilitation - 59+00 to 64+00

340	Mobilize Equipment	2d	2d	01JUL10	02JUL10
350	Install Soil Erosion Measures	1d	1d	05JUL10	05JUL10
360	Tree Clearing	5d	5d	06JUL10	12JUL10
370	Re-grade Channel	4d	4d	13JUL10	16JUL10
380	Install Double Step Rock Cross	5d	5d	19JUL10	23JUL10
390	Install Check Dams	1d	1d	26JUL10	26JUL10
400	Topsoil/Seed/Mulch	3d	3d	27JUL10	29JUL10
410	Install Trees	3d	3d	30JUL10	03AUG10
420	Install Live Stakes (If Available)	3d	3d	30JUL10	03AUG10
430	Final Restoration/Clean-up at All	8d	8d	30JUL10	10AUG10

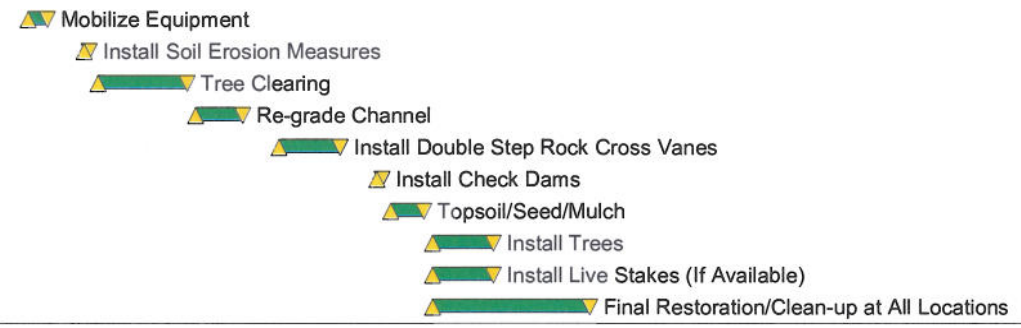

Drive Culvert - Sta 71+00

440	Mobilize Equipment	1d	1d	26JUL10	26JUL10
450	Install Cofferdam	1d	1d	27JUL10	27JUL10
460	Install 15" RCP Culvert	1d	1d	28JUL10	28JUL10
470	Backfill/Repair Drive	1d	1d	28JUL10	28JUL10
480	Remove	1d	1d	29JUL10	29JUL10



Start date	23NOV09
Finish date	10AUG10
Data date	23NOV09
Run date	12NOV09
Page number	2A
© Primavera Systems, Inc.	

Verdeterre Contracting, Inc.
Donohue Drain
Preliminary Schedule

**Donohue Drain
Road Closure Schedule**

Halsted Road (at the outlet of Pleasant Lake)	Dec 1, 2009 – Dec 16, 2009
Leytonstone Road (intermittent)	Dec 15, 2009 – Dec 24, 2009
Walnut Lake Road (near Leytonstone)	Jan 4, 2010 – Jan 7, 2010
